


Task	start	week 13	week 12	week 11	week 10	week 9	week 8	week 7	week 6	week 5	week 4	week 3	week 2	week 1
Case Studies	10													10
Prototype Building	12										10			12
Prototype Testing	10										10			0
Documentation	10												5	0
Case Study	10													0
Planning	20												2	0
Order and Manufacture Parts	20									12		3		0
Initial Build	5								5					0
prototype test	20							6	2					0
Documentation	10						8	1						0
Final Build with Finishing	10					6	3							0
Testing Software	5				3	2								0
documentation	10		7	2										0
Assembly and Test	2		5											0
Estimated Hours Remaining	154	142.1538	130.3077	118.4615	106.6154	94.76923	82.92308	71.07692	59.23077	47.38462	35.53846	23.69231	11.84615	0
Actual Hours Remaining	154	132	125	122	102	90	83	76	65	57	54	52	40	40

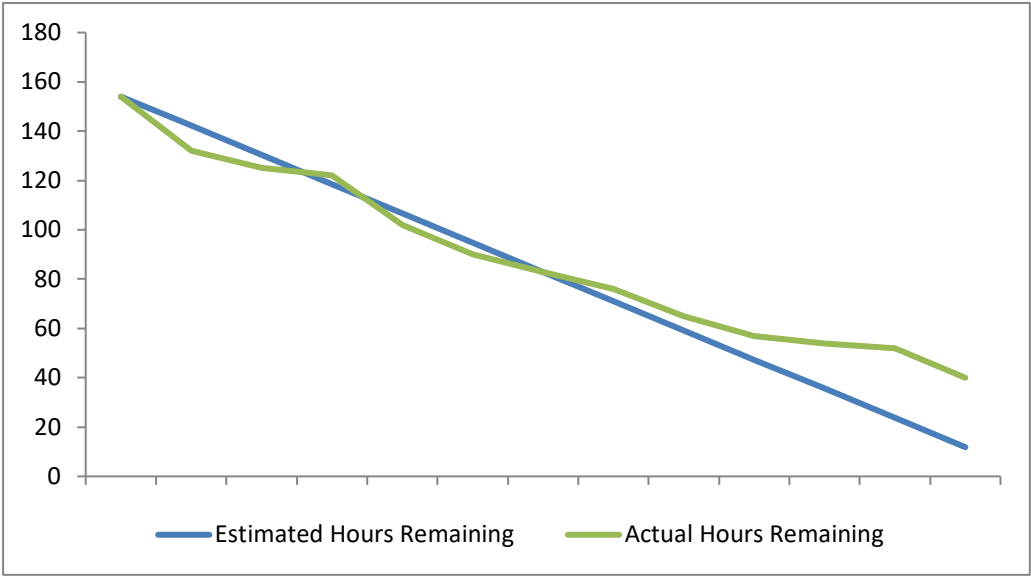

Precent Completed as of 4/20/2018
79.00%
